



2025 Street Rehabilitation Project

Project Update
June 20th, 2025

Traffic Control & One-Way Streets Project wide:

Beginning Monday, June 23rd, traffic control signage will be placed on all streets converting them to one-way streets for vehicle traffic throughout the project area. Traffic control and layout and travel routes have been included on the third page of this notice.

W Danube Rd (except from intersection to cul-de-sac): Southbound Only
East Danube Road: Northbound Only
North Danube Road: Westbound Only
Arthur Street: Southbound Only

Concrete Pavement Rehabilitation:

This week, the Contractor completed pavement saw cutting along one half of project streets. The Contractor has also completed fire hydrant replacements within the project area.

Next week, the Contractor will begin removal and rehabilitation of the existing concrete pavement marked for replacement. During the initial phase, the Contractor will complete construction of select concrete panels on one half of each street, generally following the order of: West Danube Road, North Danube Road, Arthur Street, East Danube Road. Please see the map on the second page of this notice for additional information on the first phase of concrete pavement rehabilitation.

The Contractor will first begin with concrete pavement rehabilitation in locations that do not interfere with resident driveway access. Residents will have full driveway access during this time. Once these sections have been completed and the concrete has cured, the Contractor will remove and replace any marked concrete panels in front of driveways. Residents with restricted driveway access will be permitted to utilize on-street parking adjacent to their house during this time.

Temporary Mail Service:

During In order to provide continuous and unobstructed mail service during construction, all properties within the project area will be placed on temporary mail service **beginning Tuesday, June 24th**.

Properties located north of North Innsbruck Drive will be served by individual temporary mail boxes located at the corner of North Innsbruck Drive and West Danube Road. Properties located south of North Innsbruck Drive will be served by temporary mail boxes located at the corner of North Innsbruck Drive and East Danube Road. Temporary mail box bank locations have been included in the map on the second page of this notice.

Please note that all construction scheduling is tentative, weather-dependent, and subject to change.

Project Contacts

Fridley Engineering Division

(763) 572-3554

web-StreetProjects@fridleymn.gov

Carl Lind

Project Representative

(612) 295-3990

Carl.Lind@fridleymn.gov

Construction

The Contractor's hours will be from 7:00 a.m. to 7:00 p.m., Monday-Friday. There is potential for occasional work outside of these hours with City approval.

Please keep in mind that this type of construction may generate noise, dust, mud, and be disruptive to the area. Please be patient with the Contractor and contact us if you have any concerns we can help with.

Resident Access

During construction, the City and contractor will work to minimize inconvenience to residents. That said, residents can anticipate occasional impacts to utility services and driveway access during various phases of construction. Generally, impacts to utility services are limited to short durations (hours) while driveway access may be impacted for up to 7 days during concrete work. Properties impacted by construction activity shall receive advanced written notice of such work.


For more information on construction impacts, please see the City's Construction Information and FAQs document available on the City's project webpage:






2025 Street Rehabilitation Project

Project Update
June 20th, 2025

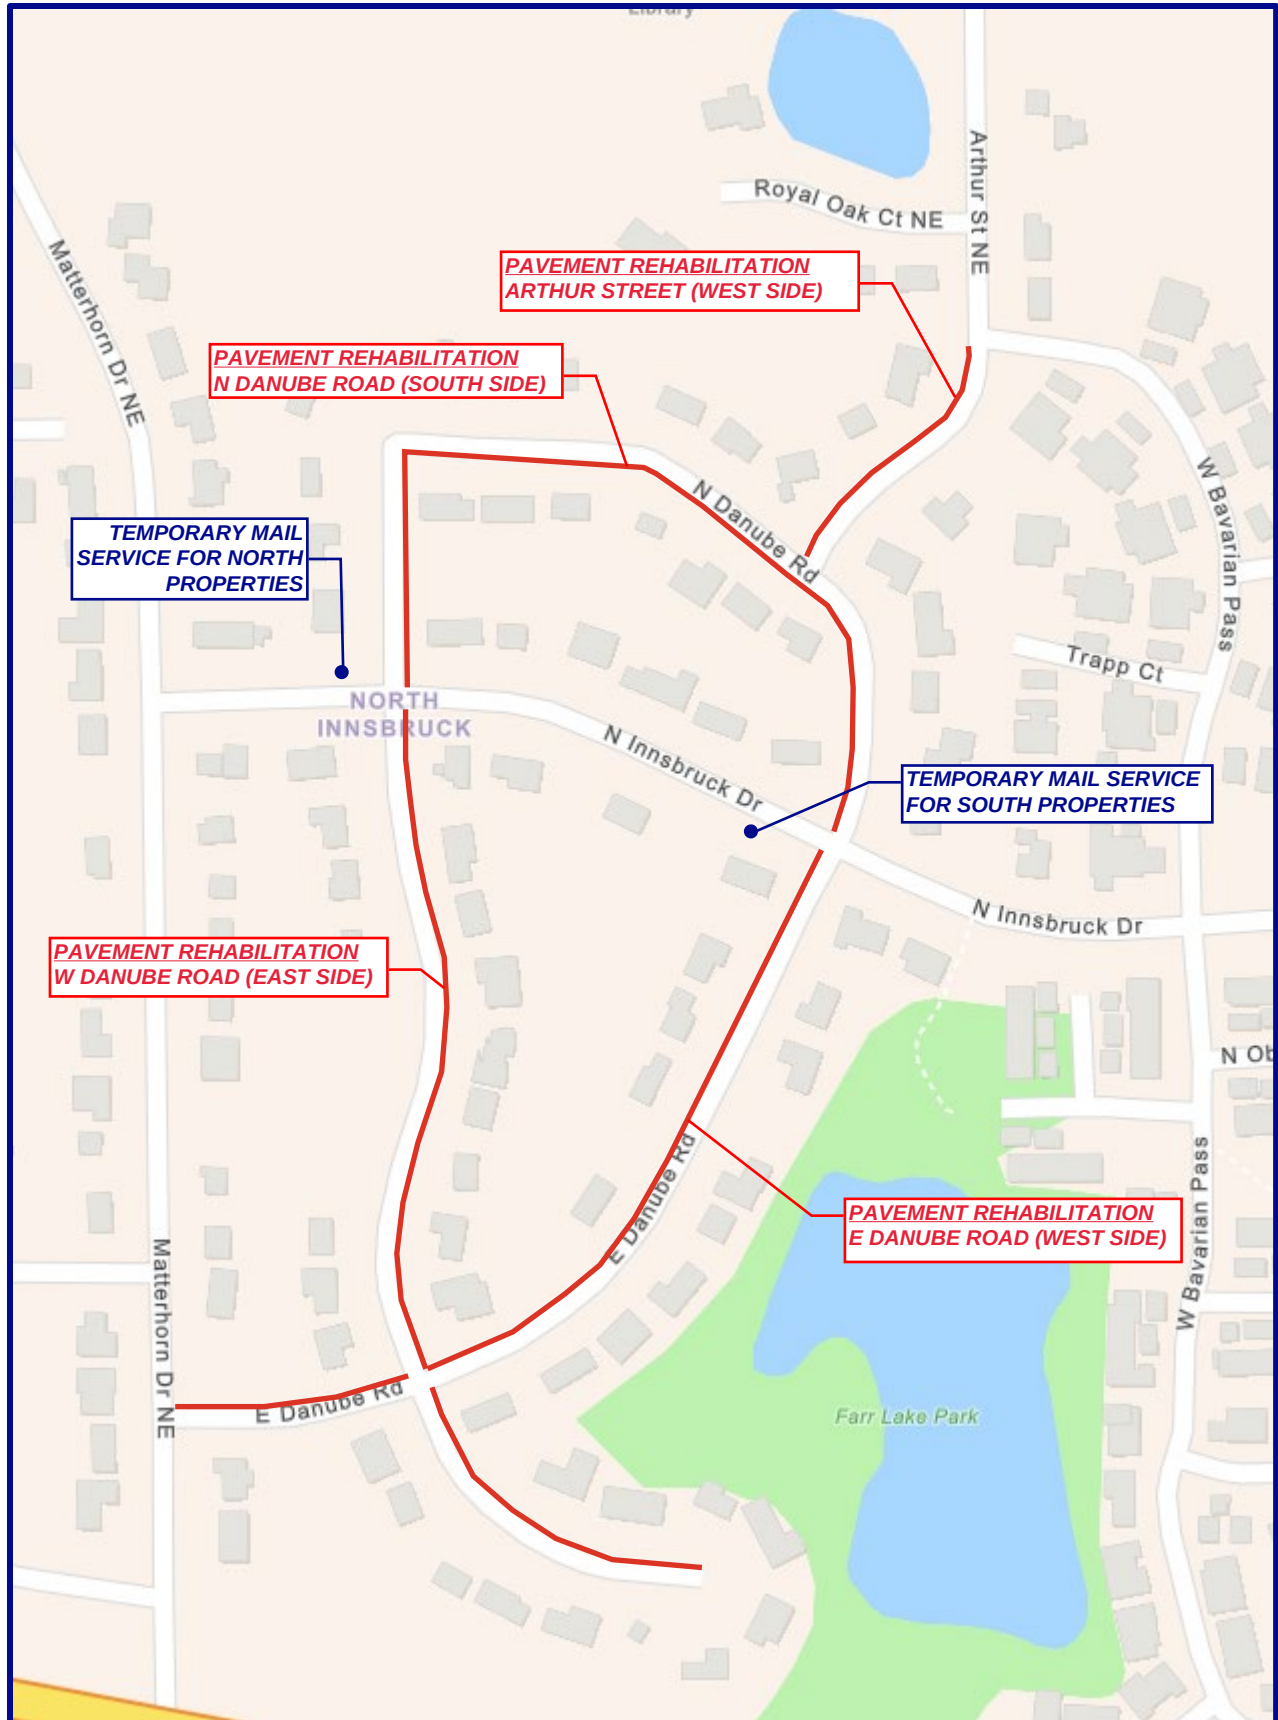

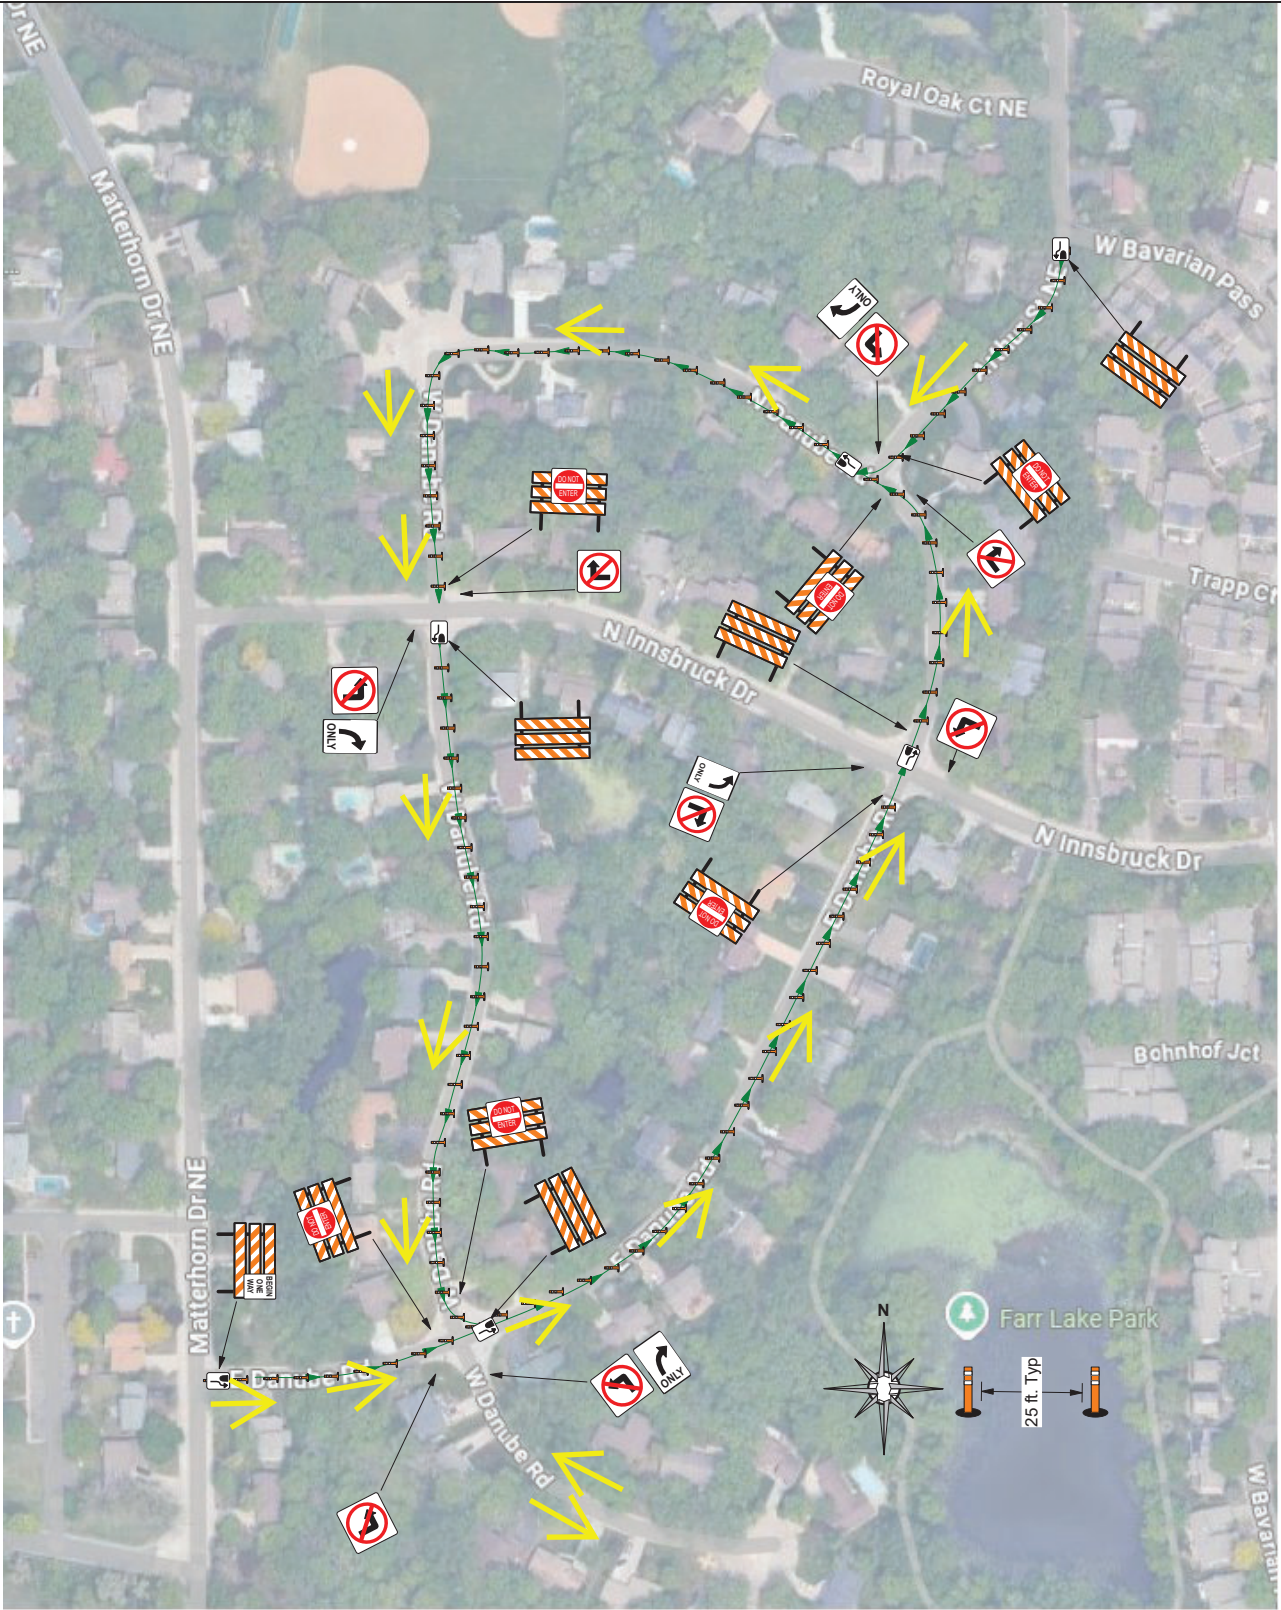



Date: 06/19/2025 Author: Trevor Johnson Project: Ti-Zack Friday 2025

Comments:

Disclaimer -

This is a proposed traffic control device layout. It has not been prepared by a professional Engineer and must be approved and accepted by the road Authority. Safety Signs LLC. does not assume any legal liability.
